


PROSPECTOR PARK DRAINAGE REVISION PROJECT CONTRACT AMENDMENT

PARKS & RECREATION
JULY 14TH, 2025



PROSPECTOR PARK DRAINAGE CHANNEL

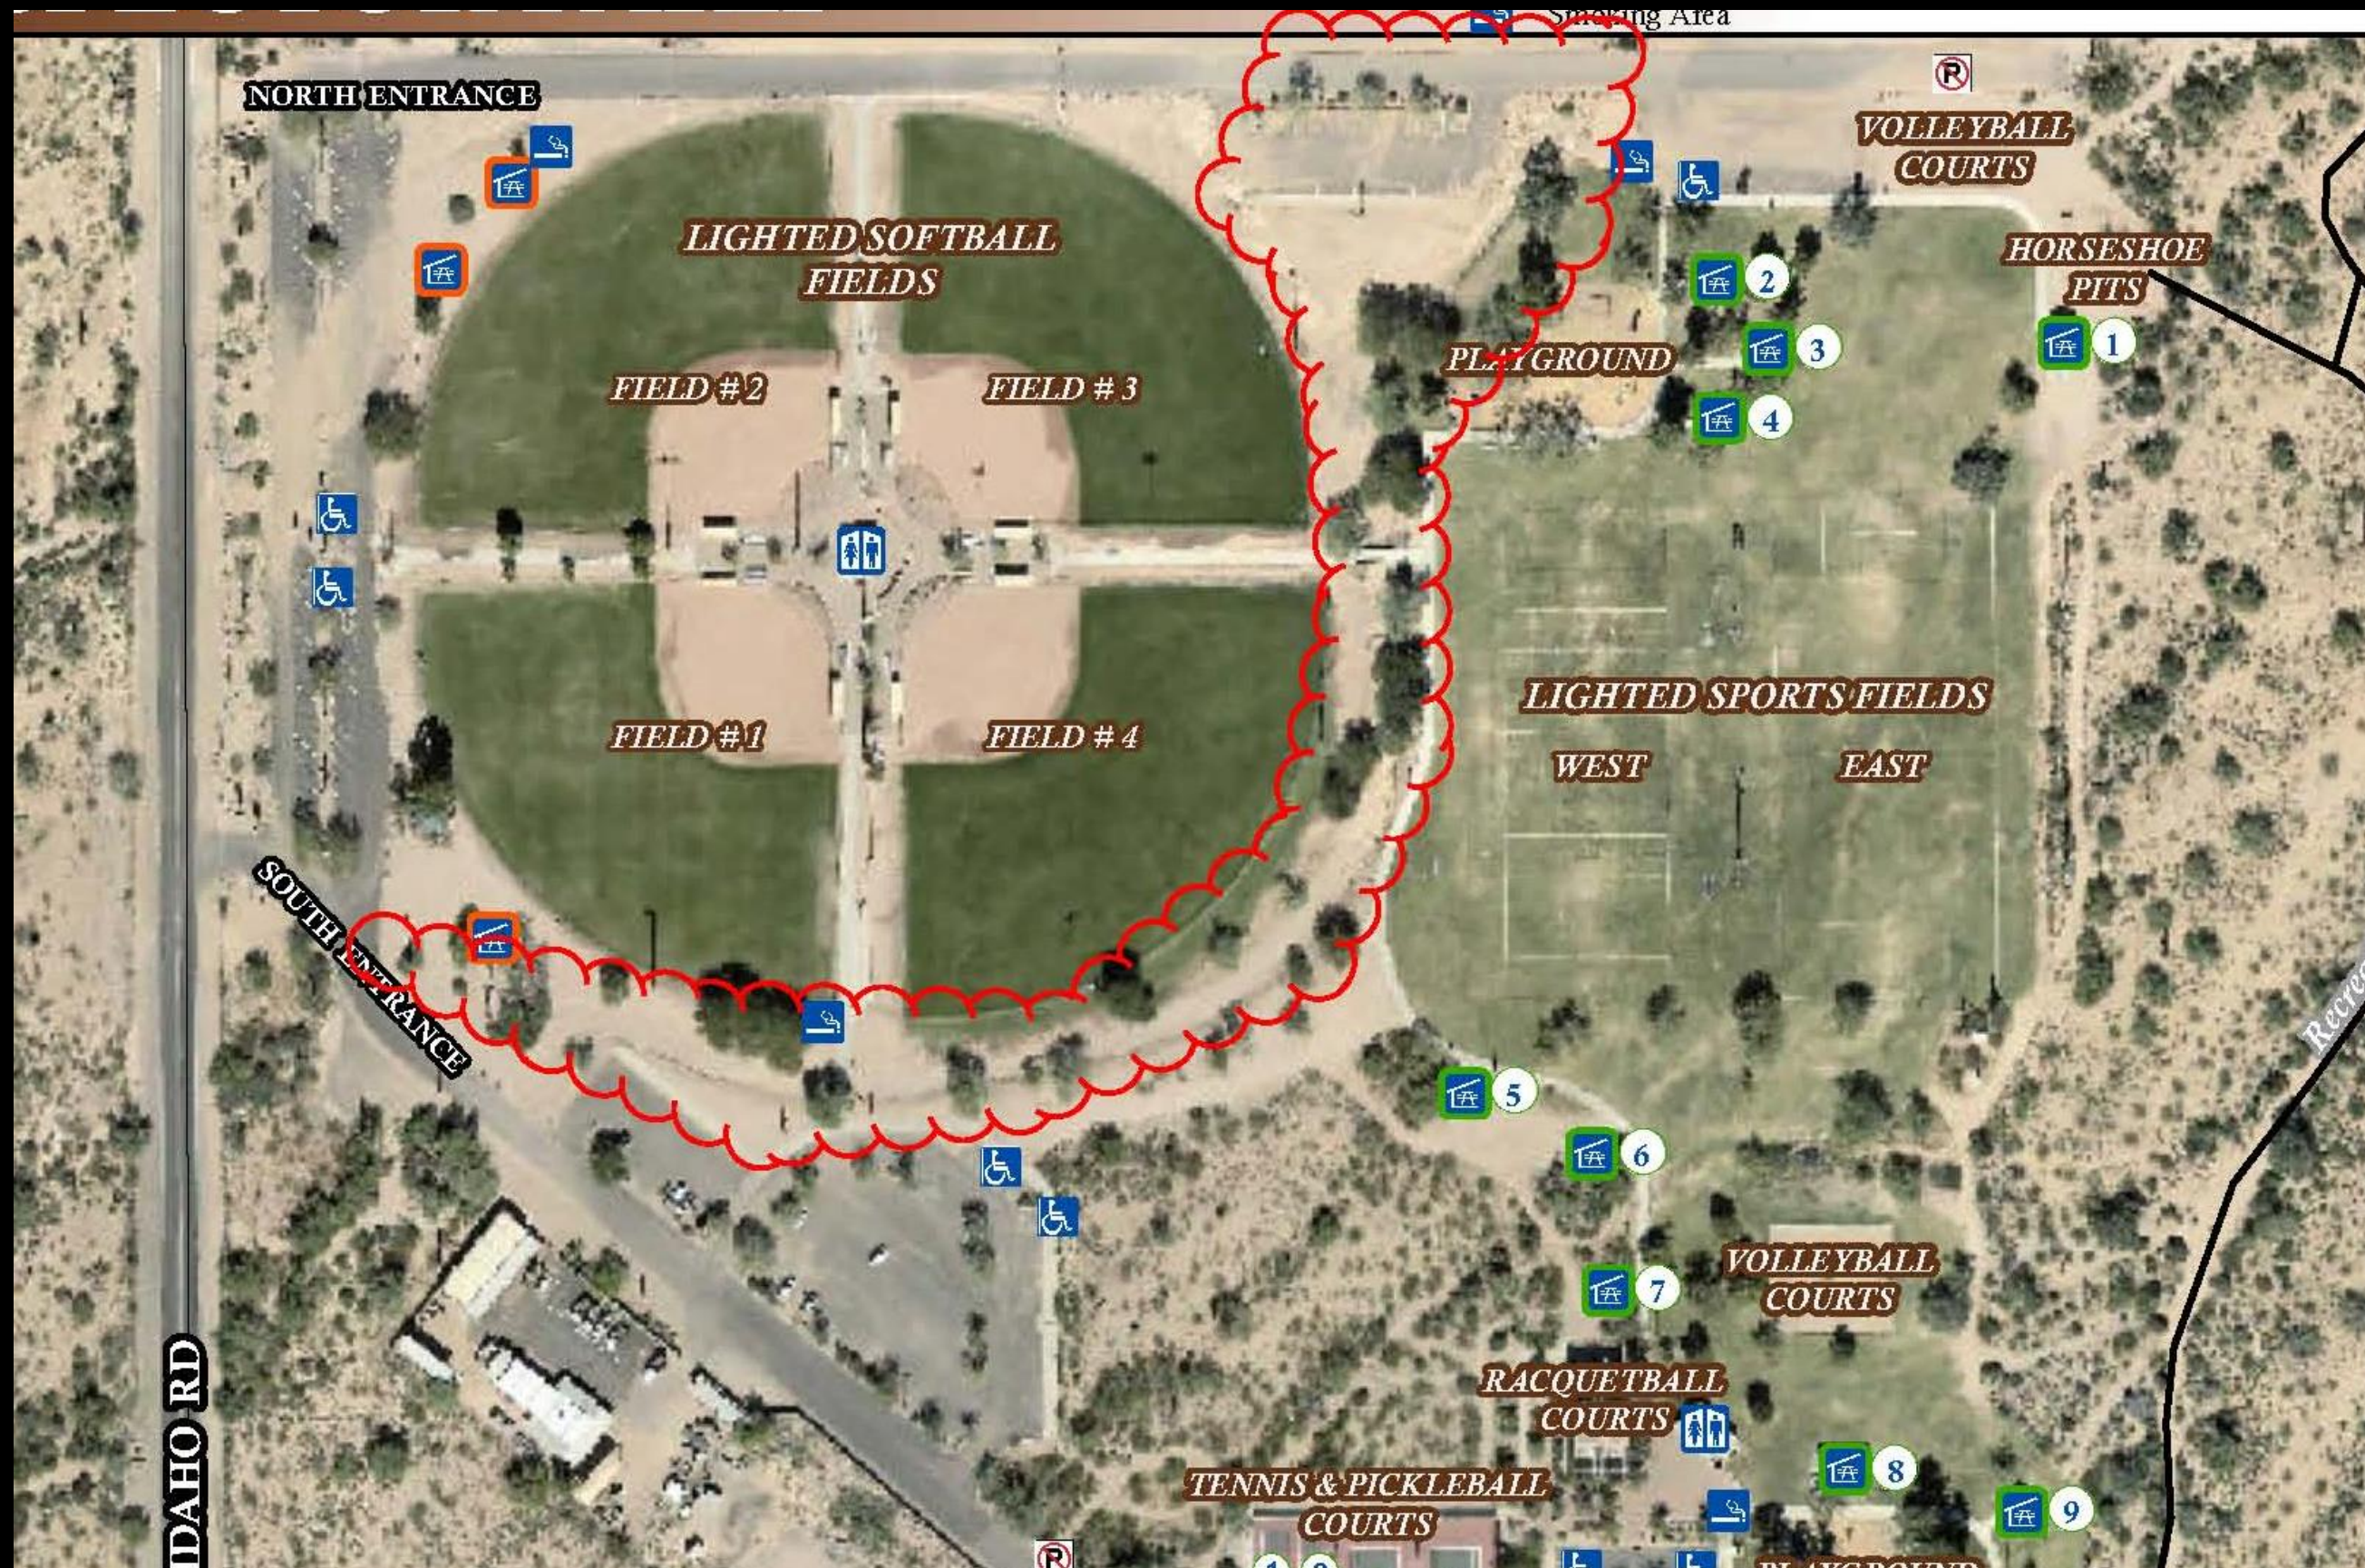

CONTRACT TERM DATE EXTENSION:

- The project has encountered several delays during the engineering, floodplain review and product submittal phase, unrelated to the contractor's performance.
- All necessary reviews and product submittals have been received and approved; however, material delivery has been further delayed.
- An amendment to the contract term end date is necessary to allow for these unforeseen delays
- There is no increase to original bid/contract amount despite engineering changes and revisions.



STAFF RECOMMENDATION:

Staff recommends amending the term end date of the contract from July 31st, 2025, to October 31st, 2025, allowing enough time to complete construction and any resulting punch-list items.



QUESTIONS?

